



Greater Brighton Economic Board

**Investment Programme Update
Report**

April 2022

Contents



Item		
1	Adur Civic Centre – Shoreham	Page 3
2	Burgess Hill Strategic Growth Programme	Page 4
3	Circus Street- Brighton	Page 6
4	Decoy Farm - Worthing	Page 7
5	Digital Catapult- Brighton	Page 8
6	Black Rock	Page 9
7	Heritage Centre Stage - Brighton	Page 11
8	New England House - Brighton	Page 12
9	New Monks Farm – Shoreham By Sea	Page 13
10	Plus X - Brighton	Page 14
11	Railway Quay - Newhaven	Page 15
12	Springman House - Lewes	Page 16
13	Teville Gate - Worthing	Page 17
14	Union Place - Worthing	Page 18
15	Valley Gardens - Brighton	Page 19
16	Western Harbour Arm – Shoreham-By-Sea	Page 20

Adur Civic Centre – Shoreham



Funding (all years)

Total LGF Funding	£1.71m
Total Public Funding	£0.0m
Total Private Funding	£9.89m
Total Other Funding	£0.00m
Total Funding	£11.60m

Outputs

Phase 1 North Site -30,000sqft of employment space

Phase 2 South Site – 987sqm of employment space and 171 residential units

What happened in the last period?

Phase 2: Public consultation on proposed development by Hyde Housing took place on 20/02/2020 and detailed design work was undertaken throughout 2021.

Planning application submitted autumn 2021

Target Milestones (Phase 2)

Planning Determined: February 2022

Start on site: April/May 2022

Completion: by Autumn 2024

Aims & Objectives

Adur District Council have led on the development of a two phase scheme for the former Council offices in Shoreham. Phase 1 involved the development of a 30,000 sqft (gross) office building which is now complete and let to local business Focus Group following £9.89m of Council investment.

For Phase 2 the Council have identified Hyde Housing as the preferred bidder for the site (Hyde Housing) and are working to finalise contracts. A planning application was submitted in August 2021 for 173 homes (100% affordable in line with Hyde Housing’s strategic partnership with Homes England) and ground floor commercial space.

Key Facts

Delivery Partners: Adur District Council, Willmott Dixon, Hyde Housing Group

Burgess Hill Strategic Growth Programme



Artist's impression

Aims & Objectives

The programme will deliver transformative change to the town, secure major growth and significant improvements in housing, jobs, infrastructure, and social and community facilities. To support the programme the following grant funding has been secured:

- **£17 million** from the Local Growth Fund (LGF) to support A2300 corridor improvements comprising an upgrade to a dual carriageway, junction improvements, and the provision of a footway and cycleway linking to the National Cycle Network.
- **£10.9 million** LGF funding for a Place and Connectivity package of sustainable transport schemes including improvements to Burgess Hill and Wivelsfield railway stations, public realm improvements, and an inter-urban cycle route between Haywards Heath and Burgess Hill.
- **£4 million** LGF and a further **£6.5 million** Housing Infrastructure Fund (HIF) to improve the Goddard's Green Waste Water Treatment works, unlocking land to develop a further 256 homes.
- Up to **£2.2 million** from the Government's Local Full Fibre Network fund and **£2 million** LGF and **£1.6 million** retained business rates to support the implementation of new digital infrastructure for Burgess Hill which in turn will stimulate the market for internet service providers.
- **£165k** from One Public Estate for design and feasibility studies to redevelop 'The Brow' and land adjacent to Burgess Hill Station.
- **£1 million** Access for All funding to improve accessibility at Wivelsfield Station.

Key Facts

Delivery Partners: Mid Sussex District Council, Homes England, West Sussex CC, Burgess Hill Town Council, Coast to Capital, Department of Transport, and developers.

Funding (all years)

LGF Funding	£33.9m
Homes England funding	£370.5m
DCMS & other digital funding	£3.8m
OPE Funding	£165k
Access for All	£1.0m
WSCC Funding	£3.34m
MSDC Funding	£3.69m
Total Public Funding	£416.39m
Total Private Investment	£643.3m
Total Funding	£1,059.7m

Following their acquisition of the Northern Arc land parcels, the Council has an approved Infrastructure Delivery Plan (IDP) with Homes England which confirms an investment of £162m in strategic infrastructure.

Outputs

5,000 new homes, a Science and Technology Park (up to 100,000m² employment space), two business parks, 15,000 new jobs (including construction jobs), a major town centre regeneration (offering retail space, commercial leisure space including a cinema and a bowling alley, a hotel as well as new homes), improvements to the A2300 corridor, a package of public realm and sustainable transport schemes, new schools, increased GP capacity, improved leisure facilities, full-fibre digital infrastructure.

What happened in the last period?

Northern Arc: Work is continuing on site with housebuilder Countryside Properties with first occupations of homes on Freeks Farm anticipated May 2022. Work is complete on the Western Link Road Roundabout with full use expected following the completion of the A2300 dualling. Homes England progressing the feasibility for the first primary school on the site. Pre-application discussions have commenced for secondary school on site. Planning application has been received for the pedestrian and cycle bridge that will link Freeks Farm with the eastern neighbourhood centre.

A feasibility study for the Centre for Outdoor Sports has been completed and next stage plans agreed with facilities to be developed for use by the public by 2025.

Place and Connectivity: Work continues delivery of the first of the MSDC Led Phase 1 schemes including public art and other public realm improvements to the underpass at Wivelsfield Railway station. A contractor has been appointed for the WSCC Phase 1 schemes in February 2022 with programmed start on site in May 2022 and completion Spring/Summer 2023. Delivery continues on Green Link (83% complete, 5.85km/7km) and Green Circle routes (98% complete, 4.45km/4.55km).

A2300 corridor improvements: Construction began in spring 2020; programme now complete with both carriageways to be opened officially on the 8th April 2022.

Employment space, The Hub: The second phase of development (a 5,000m² warehouse for Roche Diagnostics) was completed in early February. Outline planning permission for the remaining 40,000m² has been approved, and issued.

Digital Infrastructure: Works to implement the Digital Infrastructure across and around Burgess Hill, including a southern link to Brighton and a northern link via Horsham to Crawley, are well progressed. The Local Full Fibre Network (LFFN) project has now been delivered totalling 15km of dark fibre and the Burgess Hill Fibre Exchange. Customer enquiries being received and are responded to through the CNI co-operative partners.

One public estate (OPE) 7: The Brow - redevelopment of an extended Brow site in Burgess Hill will provide enhanced accommodation for the emergency and primary care services and to create space for 440 new homes (led by WSCC). Consultants Faithful and Gould have completed a draft viability study which is currently being reviewed to agree next steps.

Land adjacent to Burgess Hill station - Officers are working with key stakeholders including Network Rail and The Arch Company (the principal land-owner at the site). Review of feasibility and appraisal work is underway.

Goddards Green Waste Water Treatment Works: Phase 1 of the project has been completed delivering most of the odour reduction benefits. All the £4m LGF-funding has been spent, alongside the £6.54m HIF grant. The remainder of the project will be funded by private Southern Water investment (£13.6m).

Target Milestones — Various (project-specific).

Circus Street – Brighton



people will use the space every year. It will become a cultural and community hub, where people gather to collaborate, participate, watch and learn.

Key Facts

Delivery Partners: U+I plc (Cathedral Brighton), Brighton & Hove City Council

Funding (all years)

Total LGF Funding	£2.70m
Total Public Funding	£0.40m
Total Private Funding	£106.57m
Total Other Funding	£0.00m
Total Funding	£109.67m

Outputs

142 new homes; 387 additional jobs and 232 net additional jobs after displacement and substitution; 30,000 sq ft. office building; 450 student accommodation bed spaces; “The Dance Space” (dance studios, offices, public performance space and HQ for South East Dance); start-up workshops, retail units and restaurant; public realm to include a square and landscaped courtyards.

What happened in the last period?

All works complete. Various post Practical Completion snagging works ongoing. ical completion was achieved on both the office the office block and The Dance Space (the final 2 buildings to be completed) as well as onsite and the majority of offsite public realm works (including all public art elements). South East Dance took on the lease of The Dance Space on 16 December.

Target Milestones: All target milestones achieved

Aims & Objectives

The mix of residential, business, education and cultural occupiers on the site will bring a wide variety of people into the area, benefitting existing local businesses. Economic impact studies indicate that the development will create approximately 232 predominantly local jobs. It will generate £1 million in council tax, new business rates contributions and new homes bonuses. It would encourage student and new resident population spending in and around the site and would boost the local economy by more than £10m each year due to a multiplier effect.

The main office building will be a new centre for innovation and enterprise that will maximise the potential for linking the University’s research functions and private organisations that will cohabit in the building. This Innovation Hub will, in turn, create and support fledgling new business in the City and generate opportunities for students, graduates and university staff to work alongside SMEs and larger organisations.

The Dance Space provide a new HQ for South East Dance as well as 3 studios (one for public performances) and office space for other cultural industries. The growing artistic community in Brighton has no dedicated space for dance and it is estimated that 60,000

Decoy Farm – Worthing



Outputs

- **Phase 1:** To remediate the 7-hectare former landfill site, unlocking it for commercial development.
- **Phase 2:** To deliver up to 13,536sqm of employment floorspace by developing new commercial units to meet existing and future industrial demand.

What happened in the last period?

- Appointment of the full design team including commercial advice, surveying team, architectural team and wider suite of advisers.

Development Strategy

- Phase 2 of the development and output to deliver employment floorspace is progressing well.
- The Strategic Outline Case and Outline Business Case for the development of Decoy Farm are approved.
- Approval to progress the project through to Full Business Case in readiness for project delivery received at the Joint Strategic Committee meeting on 13 July 2021.

Target Milestones

- March 2022 launch of website and marketing material
- Summer 2022 – full planning application submitted
- Spring 2023 Commence phase 1 of the development

Aims and Objectives

An ambitious plan to upgrade an environmentally challenging but sizable plot of allocated employment land that has stood unused for over three decades. The completed project will boost employment opportunities and economic performance in the entire Coast to Capital LEP region.

Funding (all years)

Total LGF Funding	£4.84m
Total Public Funding	£4.84m
Total Private Funding	£15m
Total Funding	£25m

Key Facts

Delivery Partners: Worthing Borough Council, West Sussex County Council, Coast to Capital LEP.

Digital Catapult – Brighton



Aims & Objectives

To enable businesses to develop and exploit new products and services utilising emerging technologies (AA/VR, 5G, AI, etc), in order to improve productivity, develop better employment prospects and increase GVA in the region. The Digital Catapult Centre Brighton (DCCB) provides opportunities for start-ups and small businesses to connect with university research knowledge, work with large corporations, access innovation expertise and to engage with two core emerging technology platforms - the Immersive Lab and the 5G testbed. The 5G testbed received additional funding and the initial development and engagement activity is taking place at DCCB, hence the project date extension.

Key Facts

Delivery Partners: Wired Sussex, University of Brighton, University of Sussex, BHCC, American Express,

Funding (all years)

Total LGF Funding	£0.50m
Total Public Funding	£1.00m
Total Private Funding	£0.50m
Total Other Funding	£0.00m
Total Funding	£2.00m

Outputs

10,000 businesses receiving information about emerging technology opportunities; 1,000 businesses receiving non-financial support; 250 businesses assisted to cooperate with universities and other research institutions; 100 businesses supported to introduce new products or services to the market or the firm; 30 hackathons, boot-camps or pit-stops; and 10 in-depth collaborative R+D projects.

What happened in the last period?

On 3rd March, Digital Catapult Brighton supported the delivery of a live world-first event across 3 venues (Brighton Dome, O2 Blue Room and Metropolis Studios) that demonstrated the potential role advanced digital technologies could have in the music festival of the future.

This was the culmination of a 2-year multi-partner DCMS-supported project to provide a blueprint for how technology could play a key role in the future of festivals and music performances. Regional music venues that participated in the Alternative Stages (“virtual gigs”) strand of the project included Green Door Store, Hope & Ruin and St George’s church.

Additionally, work continues on the procurement of the specialist technical equipment required to upgrade the 5G testbed to align with BHCC’s Research & Innovation Fibre Ring project.

Target Milestones

Alternative Stages project to commence October 2021
5G Festival delivered – March 2022

Black Rock – Brighton



Aims & Objectives

The scope and outputs for the Waterfront project have now evolved in to two projects, with the agreement of the Local Enterprise Partnership. A revised series of outputs has been agreed for the Black Rock project which focus upon two key phases of enabling (underway) and future permanent development (to be progressed with a target of 2026 for completion). See alternative for summary of Waterfront project (below).

The aim of the project to regenerate the Black Rock site is now underway, with a successful planning application achieved in June 2020 and five works packages at various stages. The first two works packages, to deliver improvements to Dukes Mound junctions and begin work to the new beach boardwalk, have appointed contractors and are now completed. The Sea Wall works will complete in July 2022. The Marina Link, followed by the works to existing heritage and Kemptown Gardens will begin in May 2022.

Completion will result in full remediation of a site that has lain empty for over 40 years and will have a transport link, relocated utilities, sea defences and decontaminated site. The Development Brief for the final redevelopment of the Black Rock site is to follow the adoption of the Eastern Seafront SPD which will inform the wider objectives for the area.

The overall objective of the project is to regenerate the Black Rock site in order to unlock and de-risk this important strategic seafront site for future development. In the interim it

will also provide much needed improvements to amenity and appearance. A more developable site will be accompanied by temporary events space to support Covid recovery and a new temporary BMX pump track or Skate Park. A new play area and restored Reading room and Temple will help to begin to create a greater sense of place. Long term development will be governed by a Development Brief which will be progressed during 2021/22.

Key Facts

Delivery Partners: Brighton and Hove City Council Major Projects and Regeneration Team are leading the project.

Funding (all years)

Total LGF Funding	£12.11m - underway
Total Public Funding	£3.9m
Total Private Funding	Subject to final Business Case
Total Other Funding	£170k S106
Total Funding	£15.271m

Outputs

Outputs for the permanent Black Rock development will deliver between 163 – 354 jobs and a NPV of an estimated £86,847 - £160,259 depending upon the final composition of mixed uses.

What happened in the last period?

The 800m seafront boardwalk to provide access to Black Rock completed. The sea wall continued well and is due for completion July 2022. The Link Road final package agreed with SOS planned for May 2022. A short film about the project has been produced [Black Rock rejuvenation \(brighton-hove.gov.uk\)](https://www.brighton-hove.gov.uk/black-rock-rejuvenation)

Engagement with stakeholders continues and direct communications via website is ongoing.



The local wildlife site has been successfully relocated and is growing well in the new location. The 2nd and 3rd phases have also been completed with successful planting of seedlings taking place in December and March 2021/22. Two further short films describing this part of the project are on the BHCC website [The relocation and expansion of Black Rock's Local Wildlife Site - YouTube](#)

Target Milestones

- Phased Completion – November 2021 to May 2022 – subject to a start on site in January for the Link Road/Promenade. Link Road delays due to funding and redesign now planned for May 2022 with completion December 2022.
- New promenade and temporary surfacing for final site – March 2023.

112

Heritage Centre Stage – Brighton



Funding (all years)

Total LGF Funding	£3.00m
Total Public Funding	£25.90m
Total Private Funding	£5.70m
Total Other Funding	£0.00m
Total Funding	£34.60m

Outputs

Employment: created and/or safeguarded - 337

Businesses assisted: financial and non-financial - 624

New floor space constructed/refurbished: learning - 157 m² new floor space constructed/refurbished, Commercial - 2,652 m²

Carbon reduction 39.961 tonnes of CO₂.

What happened in the last period?

The Council’s appointed Management Contractor, Westridge Construction Limited, has completed roofing and structural remedial works to the 200-year-old Corn Exchange timber frame to secure the building envelope. The Studio theatre fibrous plaster ceiling and copper roof require replacement as they have reached the end of their useful lives and have been brought into scope with these works on-going. Finishing and completion works are progressing with the installation of the Corn Exchange oak wall boarding completed and the timber floor now being fitted. Covid-19 and possibly Brexit appear to be impacting availability of materials with longer delivery times, associated delays and increasing costs. This remains an on-going risk. IN line with Government guidance on site measures related to Covid-19 have been relaxed with visitors given the choice of wearing facemasks. Practical Completion is now anticipated in September 2022.

Target Milestones

End Date: September 2022

Aims & Objectives

New Business Model & Commercial Strategy that increases future resilience by improving commercial performance and reducing running costs:

- Enhanced contribution to Brighton’s cultural tourism by a strengthened City Centre & Cultural Quarter offer
- Returning the Royal Pavilion Estate to a world class heritage destination & protecting the heritage
- Achieving the long-term vision for both organisations
- Evidence-based improved Visitor/ Audience experience, and improved learning, access & participation).

Key Facts

Delivery Partners: Brighton & Hove City Council & Brighton Dome & Brighton Festival

New England House - Brighton



Funding (all years)

Total LGF Funding	n/a
Total Public Funding	11.1 million
Total Private Funding	n/a
Total Other Funding	n/a
Total Funding	n/a

Outputs

Upgrade building, including providing a net additional 7,090m² of new employment floor-space. Following the land deal with Legal & General on the adjacent Longley Industrial Estate, some of this City Deal floorspace output will be provided on the Longley site, with the remainder forming part of a proposed extension to New England House.

What happened in the last period?

Fire compartmentation survey work ongoing until summer. Design process will recommence once this has been completed.

Target Milestones

- Planning application: Mid 2023
- Commence works on site: Late 2024
- End Date: Mid 2026

Aims & Objectives

Upgrade and expand New England House so that it becomes a credible and highly visible hub for Greater Brighton's creative, digital and IT (CDIT) businesses.

Key Facts

New England House (NEH) is a business centre, built by the local authority in the early 1960s to provide workspace for industrial businesses. Over time, it has been subdivided into around 120 units. It is actively marketed as a centre for CDIT businesses and is much in demand for its relatively affordable workspace.

The building is in urgent need of refurbishment – especially its exterior. Under the Greater Brighton City Deal, BHCC was awarded £4.9 million in 2014 towards the refurbishment and expansion of NEH to consolidate its role as a flagship for the city's CDIT sector.

Delivery Partners: Brighton & Hove City Council

New Monks Farm - Shoreham-By-Sea



Aims & Objectives

The project is to develop a strategic employment and housing growth centre in Shoreham. Its main components are: (a) The provision of a new and improved signalised 6-arm junction on the A27 which will unlock housing and employment space by allowing access to and from the wider area and the specific development sites; (b) The building of 600 new homes and 10,000m² employment floor-space at New Monks Farm.

Key Facts

Delivery Partners: New Monks Farm Development Ltd, Highways England, West Sussex County Council (WSCC) and Adur District Council (ADC).

Funding (all years)

Total LGF Funding	£5.70m
Total Public Funding	£5.7m
Total Private Funding	£144m
Total Funding	£150m

Outputs

1. A £150 million capital investment;
2. The delivery of 600 new homes, 30% of which will be affordable;
3. 876 gross new jobs;
4. £2.8m in public sector receipts from council tax revenues, new homes bonus and new business rates; and £11.5m additional annual GVA to the Adur economy

What happened in the last period?

There is no further update for this period. Previous report is as follows:

- Housing and infrastructure development has continued at pace with a number of units completed and occupied on the site.
- Work is due to commence on the A27 roundabout in autumn 2021 for completion in late 2022.
- Ikea announced that they will not continue with their proposed new store and that they will market the site for a suitable development in September 2021

Target Milestones

Delivery of New Junction to the A27: December 2022

Completion of Development: December 2028

Plus X – Brighton



Plus X building

Aims & Objectives

The ‘Plus X’ seven storey innovation hub is a U+I Plc concept, a model they have delivered successfully elsewhere. As a key element of the comprehensive mixed-use redevelopment it provides a unique, high quality workspace model, tailored to the unique needs of Brighton’s creative and entrepreneurial businesses, particularly those designing and making physical products. It aims to be somewhere inspiring, functional, sustainable and flexible in its design. It is an innovative provision of shared workspaces and facilities that promote collaboration and facilitate serendipity. The shared spaces range from events spaces to prototyping labs, meeting rooms and cafe/break out spaces, something that attracts both small and larger tenants.

Key Facts

Delivery Partners: Brighton & Hove City Council (Delivery Body), U+I Group Plc (Developer) and University of Brighton (together the partners in the overall mixed-use development across the combined sites).

Funding (all years)

Total LGF Funding	£7.7m
Total Public Funding	£0.00m
Total Private Funding	£12m
Total Funding	£19.7m

Outputs

Contractual outputs: 4,910m² of new employment space, 517m² of high specification prototyping labs/workshops, 100 onsite jobs, £5.427m of match funding.

Non-contractual outputs: 200 other jobs, £250,000 follow-on investment, 141 businesses supported.

What happened in the last period?

Plus X remained operational and continued to grow membership. Since its opening in August 2021, the new ground floor café, Café Domenica, has proved a huge success with members and visitors. The café also provides training opportunities for young people with learning disabilities. The Brighton Research Innovation Technology Exchange programme for ambitious and established businesses primarily based in the Coast to Capital Local Enterprise Partnership region continued. Other elements of the Preston Barracks redevelopment are at an advanced stage, with several buildings at or nearing completion. The first residential blocks are due for completion and occupation in the coming months, and external works to other residential blocks continues. The University of Brighton’s adjacent development also progressed well. The new student halls on the Mithras House site were completed. Construction of the new pedestrian bridge spanning the Lewes Road continued, with the foundations on either side of the road advancing, with completion expected in the first half of 2022.

Target Milestones – Complete development End Date: Dec. 2022.

Railway Quay - Newhaven



Funding (all years)

Total LGF Funding	£1.5m
Total Public Funding	£840k (so far, mix of TF and CiL)
Total Private Funding	TBC
Total Other Funding	TBC
Total Funding	TBC

Outputs

New commercial floor-space, job creation and land remediation. Details currently being finalised.

What happened in the last period?

Flood defence works on site now completed and negotiations underway with existing tenant re: relocation. LDC has secured £1.3m from the Getting Building Fund to convert the former UTC building into a maritime and sustainable technology hub, offering education / training space and commercial facilities for SME's. This has been augmented by a commitment of £500k from LDC towards the estimated £1.8m project costs. Lease negotiations with DfE are being finalised and hopeful of taking possession in early 2022. A final layout plan is being prepared and it is planned to undertake an Expression of Interest process to elicit appropriate commercial partners for the project.

Phase 1 of Railway Quay is now complete, funded through the Towns Fund and CiL to deliver The Sidings - offering new visitor, community and sustainability facilities, including a café and a base for the local gig rowing club, as well as an active travel hub. Funding has been secured from DfT towards a trial of e-cargo bikes to be based at the site with orders now having been placed.

Target Milestones

End Date: TBC.

Aims & Objectives

The Newhaven Enterprise Zone (EZ) is a cross-agency that aims to shift the town towards a higher-value economy over the next 25 years. The EZ covers eight key strategic sites (79ha) in a mixture of public and private ownerships, offering a mix of greenfield sites and the opportunity to develop, refurbish and intensify economic activity across a number of brownfield sites formerly used by heavy industry. The focus of the EZ is on growing the emerging 'clean, green and marine' sectors in particular. Over the 25-year lifespan of the EZ, it is estimated that 55,000m² of new commercial floor-space will be created, 15,000m² of existing commercial floor-space will be refurbished. This will create / sustain up to 2,000 FTE jobs.

Key Facts

Delivery Partners: Lewes District Council.

Springman House – Lewes



Aims & Objectives

The project involves the formation of new fire and ambulance station facilities. A key project aim is to deliver modern new premises for both services.

Key Facts

Delivery Partners: Lewes District Council are the lead delivery body in partnership with East Sussex Fire & Rescue Service (ESFRS), Sussex Police and the South East Coast Ambulance Service.

Funding (all years)

Total LGF Funding	£2.00m
Total Public Funding	£4.34m
Total Private Funding	£0.00m
Total Other Funding	£0.00m
Total Funding	£6.34m

Outputs

By enabling the development of a new blue light facility on the site of Springman House, this project will unlock the North Street Quarter scheme - a major, strategic mixed-use development in Lewes. Relocating the Community Fire Station from its existing premises on North Street, Lewes will enable the delivery of new homes and commercial floor-space through the North Street Quarter (NSQ) regeneration scheme, and enable Lewes’ “blue light” services to be co-located.

What happened in the last period?

There has been no update since the last period. Previous update is as follows:

Following the purchase of the site by Lewes District Council, plans were drawn up with the East Sussex Fire and Rescue Service Sussex Police and the South East Coast Ambulance Service. NSQL, the majority landowner at the NSQ site, has now sold its land to the developer – Human Nature. In December 2020, the Council’s Cabinet agreed heads of terms for the sale of its own land to this same developer in order that it can comprehensively redevelop the site. Human Nature has confirmed that it will submit a new planning application for the NSQ and the Council is now liaising with the developer to understand its plans and timescales for the site, including the fire station.

Target Milestones

End Date: To be confirmed, subject to Human Nature’s programme including planning.

Teville Gate - Worthing



Teville Gate House Construction 12/12/2019

Aims & Objectives

Teville Gate (TG) forms part of the Worthing Central Programme (Phase 1) to transform key brownfield sites in Worthing town centre. This project will facilitate the redevelopment of the site by undertaking site preparation works, consisting of the demolition of all buildings within the redline and provision of a temporary surface car park. Thereafter the Council will continue to support the freeholders, Mosaic Global Investments (Mosaic) and Hanson Development to develop out the scheme for office, residential and commercial.

Key Facts

Delivery Partners: Worthing Borough Council, Mosaic Global Investments, Coast to Capital LEP, Hanson Developments & HMRC, Homes England

Funding (all years)

Total LGF Funding	£2.09m
Total Public Funding	£2.0m
Total Private Funding	£79m (wider site) £32m (Teville Gate House)
Total Funding	£81.00m

Outputs

(a) 375 new homes (b) 3,410sqm of commercial floor-space (restaurants, cafes and on-site gym) (c) 6,740sqm of retail floor-space (state of the art supermarket) (d) 493 gross jobs (net jobs 314) (e) Modern car parking infrastructure (over 160 spaces for residents and visitor use) (f) New public realm (approx. 4,000sqm, creating an improved public corridor from Worthing station to the town centre). 70,000sqft office building at Teville Gate House for HMRC.

What happened in the last period?

- Site acquired by Worthing Borough Council for redevelopment in August 2021
- Development Strategy and approach involving joint investment with London & Continental Railways confirmed in December 2021
- March 2022 Development Partner agreed by JSc Committee – Hyde Housing Group.

Target Milestones

Spring/ summer – finalise agreements with Hyde Housing Group.

Winter 2022 – planning process commence

Spring 2023 – planning application submitted.

Union Place - Worthing



Aims & Objectives

Union Place (UP) forms part of the Worthing Central Programme (Phase 1) to regenerate key brownfield sites in Worthing town centre. The Council has entered into a land pooling agreement for the site with partners London and Continental Railways (LCR). The partners have prepared a development strategy for the sites which has been approved at JSC. The development strategy could include direct delivery or selling the consented scheme to a developer.

Key Facts

Delivery Partners: Worthing Borough Council (WBC), London & Continental Railways, Coast to Capital LEP.

Funding

Total LGF Funding	£3.60m
Total Public Funding	£5m
Total Private Funding	£31.4m
Total Other Funding	TBC
Estimated GDV	£70m

Outputs

- 169 - New Homes – 30% affordable
- 610sqm - Commercial Space
- 90 - Guest room Hotel
- 3 /4 Screen – Cinema
- 1072sqm- Flexible Cultural Space
- 245 – Parking spaces


What happened in the last period?

- S106 agreement drafted and formal planning permission issued
- Roffey Homes Agreed as Development Partner on the site

Target Milestones

- Finalise JV agreement – June 2022
- Detailed/ revised matters planning application due – autumn 2022
- Commence on site spring 2023

Valley Gardens Phase 3 – Brighton

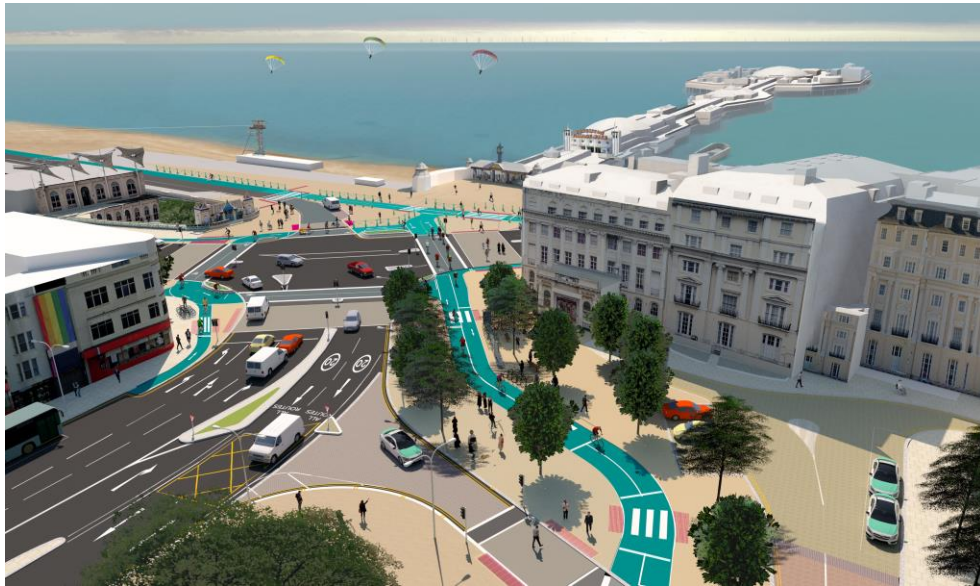

Proposed scheme

Aims & Objectives

Simplification of traffic network, provision of 'public transport corridor' to the west with general traffic on the western corridor. Enhanced public realm, gardens and materials throughout. The scheme aims to contribute to improved air quality, safety, accessibility, connectivity, improve efficiency and upgrade signals at junctions. Reduce street clutter and provide enhanced greenspace for public enjoyment.

Key Facts

Delivery Partners: C2C Local Enterprise Partnership

Outputs

Match Funding (BHCC) £1.712m, Local Funding £0.414m, Total resurfaced roads - 1,588m, Total length of cycle ways - 670m.

Funding (all years)

Total LGF Funding	£6.00m
Total Public Funding	£1.84m
Total Private Funding	£0.0m
Total Other Funding	£0.00m
Total borrowing	£5.00m
Total Funding	£12.84m

What happened in the last period?

Following the third public consultation exercise for Valley Gardens Phase 3 which completed in late 2020, and further stakeholder engagement the final General Highway Arrangement was agreed by ETS Committee in January 2022. Furthermore, the additional budget requirement needed to deliver the project was approved by Policy & Resources Committee which would be acquired through borrowing. Cost estimates have increased due to rising construction costs and additional stakeholder infrastructure included in the plan, such as those required for sustainable events and cycling. The construction contract procurement will commence in spring 2022 and be completed by autumn 2022. Construction to complete spring 2024.

Target Milestones

End Date: Spring 2024

Western Harbour Arm – Shoreham-By-Sea



Proposed scheme

Aims & Objectives

A new flood defence wall and cycle path to be constructed in Shoreham adjacent to the A259 on Brighton Road where the flood defence is at its most vulnerable point for flooding. ADC purchased a 3.5m strip of land off Sussex Yacht Club through grant funding from Coast 2 Capital LEP. The sale of the land would enable the yacht club to build a new club house and allow the council to demolish the redundant club house where the new flood wall will be located.

Key Facts

Delivery Partners: Adur District Council (ADC), Environment Agency and Sussex Yacht Club, Shoreham Harbour Partnership.

Funding (all years)

Total LGF Funding:	£3.50m
Total Public Funding:	£1.14m
Total Private Funding	£0.00m
Total Other Funding:	£0.00m
Total Funding:	£4.64m

Outputs

- Flood defence scheme to protect residents and businesses
- Cycle path
- New yacht club for Shoreham.

What happened in the last period?

- Demolition of redundant Yacht Club October/November 2021
- Continued pluvial and fluvial modelling to inform design

Target Milestones

- Commencement of Flood Defence construction 2022
- Completion autumn 2022
